




Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float	2003												2004											
										J	Y	M	D	2003	S	P	N	D	F	M	A	M	J	J	A	S	O	N	D	P			
94	Exterior Brick Veneer	19	19	0	08JUL03	01AUG03	04MAY04	28MAY04	215																							Exterior Brick Veneer	
105	Roofing/Flashing & Sheetmetal	17	17	0	08JUL03	30JUL03	07MAY04	31MAY04	218																							Roofing/Flashing & Sheetmetal	
102	Install Curtainwall	2	2	0	01AUG03	04AUG03	28MAY04	31MAY04	215																							Install Curtainwall	
103	Install Aluminum Windows	2	2	0	01AUG03	04AUG03	28MAY04	31MAY04	215																							Install Aluminum Windows	
107	Sprinkler Rough 1st Floor	16	16	0	19AUG03	09SEP03	14APR04	05MAY04	171																							Sprinkler Rough 1st Floor	
108	Sprinkler Rough 2nd Floor	16	16	0	09SEP03	30SEP03	05MAY04	26MAY04	171																							Sprinkler Rough 2nd Floor	
109	Sprinkler Stand Pipe	4	4	0	30SEP03	03OCT03	26MAY04	31MAY04	171																							Sprinkler Stand Pipe	

## **Building C - Classrooms**

116	Footers & Piers	68	3	96	09JAN03A	01MAY03	09JAN03A	06DEC02	-104		Footers & Piers	
120	Underslab Utilities	10	1	90	21JAN03A	08MAY03	21JAN03A	19FEB03	-56		Underslab Utilities	
117	Pedestals	3	0	100	21JAN03A		21JAN03A				Block Wall Below Grade	
118	Block Wall Below Grade	5	5	0	29APR03	05MAY03	10FEB03	14FEB03	-56		Backfill Foundations	
119	Backfill Foundations	2	2	0	06MAY03	07MAY03	17FEB03	18FEB03	-56		Underslab Stone/Insulation	
121	Underslab Stone/Insulation	2	2	0	09MAY03	12MAY03	20FEB03	21FEB03	-56		Slab on Grade	
122	Slab on Grade	10	10	0	13MAY03	26MAY03	24FEB03	07MAR03	-56		Erect Steel & Metal Deck	
126	Erect Steel & Metal Deck	11	11	0	02JUN03*	16JUN03	10MAR03	24MAR03	-60		Set Masonry Door Frames	
129	Set Masonry Door Frames	4	4	0	16JUN03	19JUN03	09APR03	14APR03	-48		Set Roof Drains & Curbs	
138	Set Roof Drains & Curbs	5	5	0	16JUN03*	20JUN03	06MAY04	12MAY04	232		Slab on Metal Deck	
124	Slab on Metal Deck	11	11	0	16JUN03	30JUN03	17MAY04	31MAY04	239		Set Fire Dampers & Sleeves	
123	Set Fire Dampers & Sleeves	3	3	0	16JUN03	18JUN03	27MAY04	31MAY04	247		Exterior CMU Backup& Stair C	
130	Exterior CMU Backup& Stair C	6	6	0	19JUN03	26JUN03	14APR03	21APR03	-48		Exterior Metal Stud & Sheath	
134	Exterior Metal Stud & Sheath	16	16	0	26JUN03	18JUL03	21APR03	12MAY03	-48		Interior CMU Partitions	
132	Interior CMU Partitions	4	4	0	26JUN03	01JUL03	26MAY04	31MAY04	238		Interior Metal Studs	
135	Interior Metal Studs	0	0	0	18JUL03*		12MAY03		-48		Mechanical Rough	
141	Mechanical Rough	21	21	0	18JUL03	15AUG03	16MAR04	13APR04	172		Exterior Brick Veneer	
131	Exterior Brick Veneer	22	22	0	18JUL03	18AUG03	14APR04	13MAY04	193		Sprinkler Rough 1st Floor	
142	Sprinkler Rough 1st Floor	13	13	0	15AUG03*	02SEP03	13APR04	29APR04	172		Roofing/Flashing & Sheetmetal	
139	Roofing/Flashing & Sheetmetal	13	13	0	18AUG03	03SEP03	13MAY04	31MAY04	193		Install Aluminum Windows	
137	Install Aluminum Windows	6	6	0	18AUG03	25AUG03	24MAY04	31MAY04	200		Sprinkler Stand Pipe	
144	Sprinkler Stand Pipe	2	2	0	02SEP03	03SEP03	29APR04	30APR04	172		Sprinkler Rough 2nd Floor	
143	Sprinkler Rough 2nd Floor	11	11	0	02SEP03	16SEP03	17MAY04	31MAY04	184			

### **Building D - Classrooms**

Start Date  
Finish Date  
Data Date  
Run Date



ED05

MM#17 4/29/03

EDiS 18 Nov 2002 Schedule

with Total Float Bar Shown

Sheet 2 o

Dat

## Revision


\_\_\_\_\_

Approved

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float	2003												2004											
										J	F	M	A	M	J	J	A	S	O	N	D												
158	Erect Steel & Metal Deck	11	11	0	17JUN03*	01JUL03	24MAR03	07APR03	-61	▲	■	▲	■	▲	■	▲	■	▲	■	▲	■	▲	■	▲	■	▲	■	▲	■	▲	■		
166	Exterior Metal Stud & Sheath	16	16	0	01JUL03	23JUL03	21APR03	12MAY03	-51	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
170	Set Roof Drains & Curbs	6	6	0	01JUL03	09JUL03	05MAY04	12MAY04	220	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
161	Set Masonry Door Frames	4	4	0	01JUL03	07JUL03	06MAY04	11MAY04	221	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
156	Slab on Metal Deck	11	11	0	01JUL03	16JUL03	17MAY04	31MAY04	228	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
155	Set Fire Dampers & Sleeves	3	3	0	01JUL03	03JUL03	27MAY04	31MAY04	236	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
162	Exterior CMU Backup& Stair D	6	6	0	07JUL03	14JUL03	11MAY04	18MAY04	221	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
171	Roofing/Flashing & Sheetmetal	13	13	0	10JUL03*	28JUL03	13MAY04	31MAY04	220	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
164	Interior CMU Partitions	10	10	0	14JUL03	25JUL03	18MAY04	31MAY04	221	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
167	Interior Metal Studs	0	0	0	23JUL03*		12MAY03		-51	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
173	Mechanical Rough	21	21	0	23JUL03	20AUG03	02APR04	30APR04	182	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
163	Exterior Brick Veneer	16	16	0	23JUL03	13AUG03	03MAY04	24MAY04	203	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
169	Install Aluminum Windows	6	6	0	13AUG03	20AUG03	24MAY04	31MAY04	203	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
174	Sprinkler Rough 1st Floor	11	11	0	03SEP03	17SEP03	30APR04	14MAY04	172	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
175	Sprinkler Rough 2nd Floor	11	11	0	17SEP03	01OCT03	14MAY04	28MAY04	172	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		
176	Sprinkler Stand Pipe	2	2	0	01OCT03	02OCT03	28MAY04	31MAY04	172	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■		


### Building E - Classrooms

184	Underslab Utilities	10	0	100	12MAY03A		12MAY03A			▲	■	▲	■	▲	■	▲	■	▲	■	▲	■	▲	■	▲	■	▲	■	▲	■	▲	■
180	Footers & Piers	5	5	0	05MAY03	09MAY03	10DEC02	16DEC02	-104	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
181	Pedestals	3	3	0	12MAY03	14MAY03	06MAR03	10MAR03	-47	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
182	Block Wall Below Grade	5	5	0	15MAY03	21MAY03	11MAR03	17MAR03	-47	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
183	Backfill Foundations	2	2	0	22MAY03	23MAY03	18MAR03	19MAR03	-47	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
185	Underslab Stone/Insulation	2	2	0	26MAY03	27MAY03	20MAR03	21MAR03	-47	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
186	Slab on Grade	10	10	0	28MAY03	10JUN03	24MAR03	04APR03	-47	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
190	Erect Steel & Metal Deck	11	11	0	01JUL03*	16JUL03	07APR03	21APR03	-61	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
198	Exterior Metal Stud & Sheath	16	16	0	16JUL03	06AUG03	21APR03	12MAY03	-61	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
202	Set Roof Drains & Curbs	6	6	0	16JUL03	23JUL03	05MAY04	12MAY04	210	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
193	Set Masonry Door Frames	4	4	0	16JUL03	21JUL03	11MAY04	14MAY04	214	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
188	Slab on Metal Deck	11	11	0	16JUL03	30JUL03	17MAY04	31MAY04	218	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
187	Set Fire Dampers & Sleeves	3	3	0	16JUL03	18JUL03	27MAY04	31MAY04	226	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
194	Exterior CMU Backup& Stair E	7	7	0	21JUL03	29JUL03	14MAY04	24MAY04	214	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
191	Erect Stair E 105	6	6	0	29JUL03	05AUG03	24MAY04	31MAY04	214	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
196	Interior CMU Partitions	4	4	0	29JUL03	01AUG03	26MAY04	31MAY04	216	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
199	Interior Metal Studs	0	0	0	06AUG03*		12MAY03		-61	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
205	Mechanical Rough	21	21	0	06AUG03	03SEP03	02APR04	30APR04	172	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
195	Exterior Brick Veneer	20	20	0	06AUG03	02SEP03	16APR04	13MAY04	182	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
203	Roofing/Flashing & Sheetmetal	13	13	0	02SEP03*	18SEP03	13MAY04	31MAY04	182	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
201	Install Aluminum Windows	6	6	0	02SEP03	09SEP03	24MAY04	31MAY04	189	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■
206	Sprinkler Rough 1st Floor	11	11	0	03SEP03	17SEP03	30APR04	14MAY04	172	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■	▼	■



Start Date  
Finish Date  
Data Date  
Run Date

18NOV02  
22OCT04  
29APR03  
FEB08 11:28



ED05


MM#17 4/29/03

EDiS 18 Nov 2002 Schedule


### with Total Float Bar Shown

Sheet 4 c

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	Late Start	Late Finish	Total Float
260	Interior Metal Studs	0	0	0	12SEP03*		02JUN03		-73
255	Exterior CMU Backup	14	14	0	18SEP03	07OCT03	25MAR04	13APR04	135
256	Exterior Brick Veneer	16	16	0	08OCT03	29OCT03	14APR04	05MAY04	135
257	Interior CMU Partitions	31	31	0	08OCT03	19NOV03	19APR04	31MAY04	138
267	Sprinkler Rough 1st Floor	30	30	0	23OCT03	03DEC03	16APR04	27MAY04	126
262	Install Curtainwall/Windows	18	18	0	30OCT03	24NOV03	06MAY04	31MAY04	135
264	Roofing/Flashing & Sheetmetal	18	18	0	30OCT03*	24NOV03	06MAY04	31MAY04	135
268	Sprinkler Stand Pipe	2	2	0	04DEC03	05DEC03	28MAY04	31MAY04	126

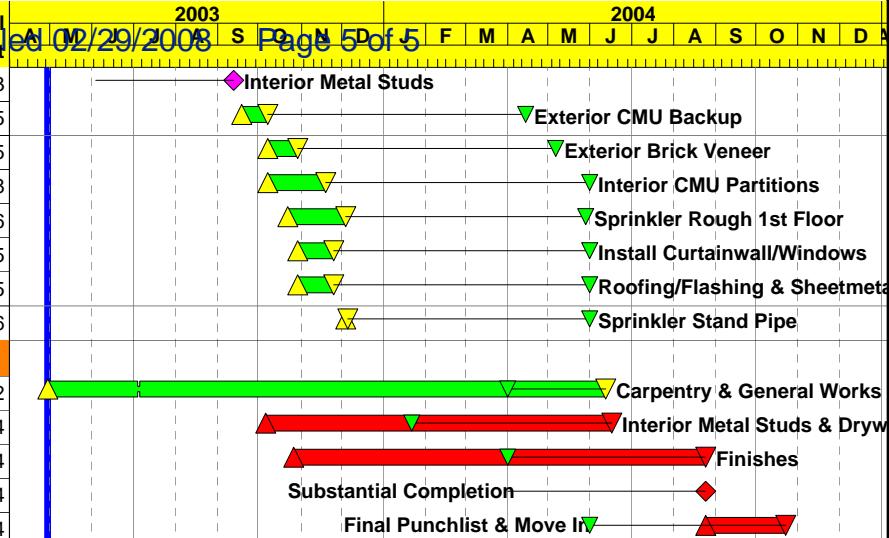

Generalized Performance									
273	Carpentry & General Works	293	293	0	29APR03*	11JUN04	14FEB03	31MAR04	-52
272	Interior Metal Studs & Drywall	182	182	0	06OCT03*	15JUN04	12MAY03	21JAN04	-104
276	Finishes	217	217	0	27OCT03	24AUG04	02JUN03	31MAR04	-104
277	Substantial Completion	0	0	0		24AUG04		31MAR04	-104
278	Final Punchlist & Move In	43	43	0	25AUG04*	22OCT04	01APR04	31MAY04	-104



ED05

Sheet 5 of 5

EDiS 18 Nov 2002 Schedule

with Total Float Bar Shown
